Technical Site Visit Report

Prepared for: Kiran Nag N J_BDA layout_6.20kWp_Microinverter

PROJECT INFORMATION

Report Number	ESV-2026-0243
Project ID	7K61GRYF
Project Name	Kiran Nag N J_BDA layout_6.20kWp_Microinverter
Project Sector	Residential
Project Type	With Subsidy
Sales Lead	Hariom
Site Address	No 727 KEERTHI Banashankari 6th stage 1st block BDA layout Bangalore-61
GPS Coordinates	12.89648020118124, 77.52403050202008
Google Maps	https://www.google.com/maps?q=12.896480201181241,77.52403050202008
Visit Date	2026-11-04
Visited By	Charan
Revision	Rev 0

CLIENT INFORMATION

Client Name	Kiran Nag N J
Contact	98803 33803

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	6.2
Sanction Load (kW)	10
Module Make & Capacity	Premier DCR Bi-facial and 620Wp
Module Length (mm)	2382
Module Width (mm)	1134

Number of Panels	10
Inverter Type	Micro
Inverter Brand	Enphase IQ8P
Number of Inverters	10
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	N/A	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	No	-
5	Did you discuss the location of the earth pits with the customer?	Earthing work has already completed.	-
6	Where is the Internet Router located?	In first floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	Full	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*HDGI structure*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	N/A	-

#	Question	Answer	Notes
13	What is the height of the building and how many floors does it have?	15m with G+4 Floors	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	Less than 50m	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	No	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	No	-
11	Is there space available to dig DC, AC and LA earth pits?	No	*Earthing work has already completed.*
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	N/A	-
13	In case of elevated structures, is an LA extension provided at the far end?	No	-
14	In case of elevated structures, is it with or without grouting?	With Grouting	-
15	Are there any challenges with respect to Installation and Maintenance activities?	No	-
16	Are there any safety risks associated with accessing the roof for installation?	No	-
17	Is space present in rooftop to store the panels?	Horizontally sleeping	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
19	Is ventilation available in the battery location?	N/A	-
20	Is Battery wall mounted or stand mounted?	N/A	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	N/A	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 2000, width: 500	-
23	Provide the dimension for earth pits location (L x W of available space).	N/A	-
24	Is LAN cable under customer scope?	No	-
25	Is there any shadow that affects the solar installation?	No	-

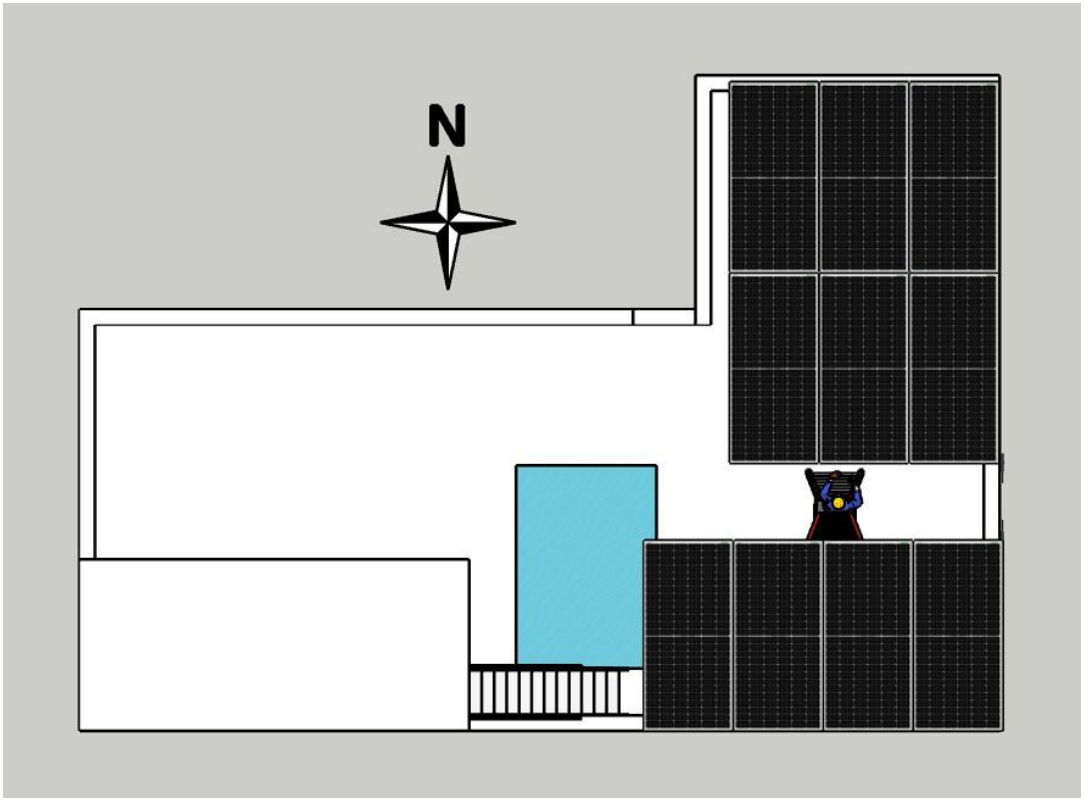
#	Question	Answer	Notes
26	Is there any trench work to be done to carry the AC cable to the meter location?	No	-


PHOTO DOCUMENTATION


Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout



N

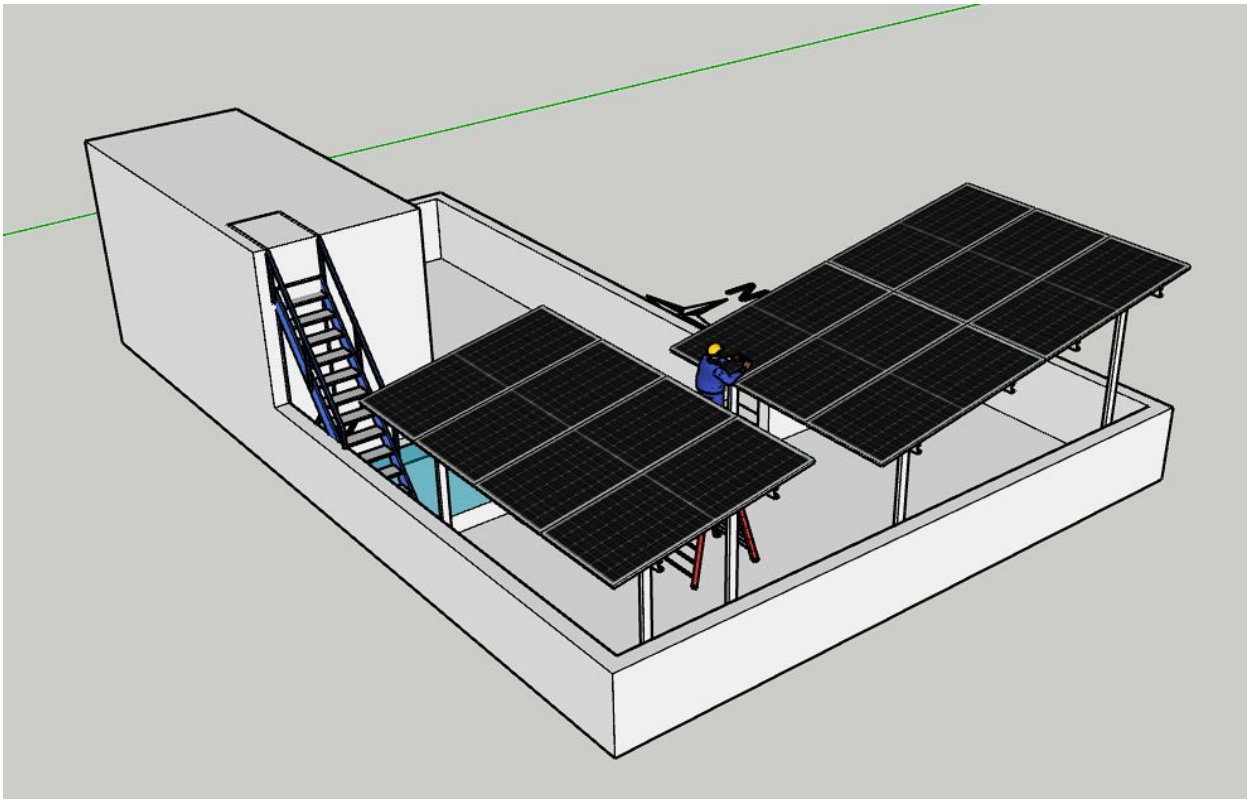

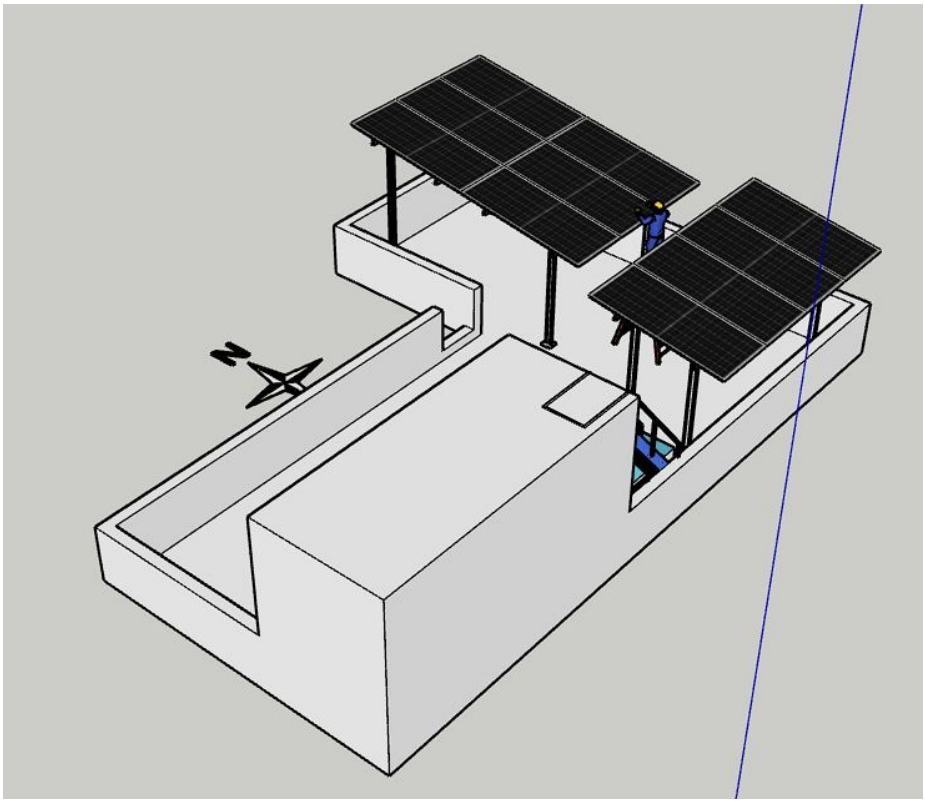


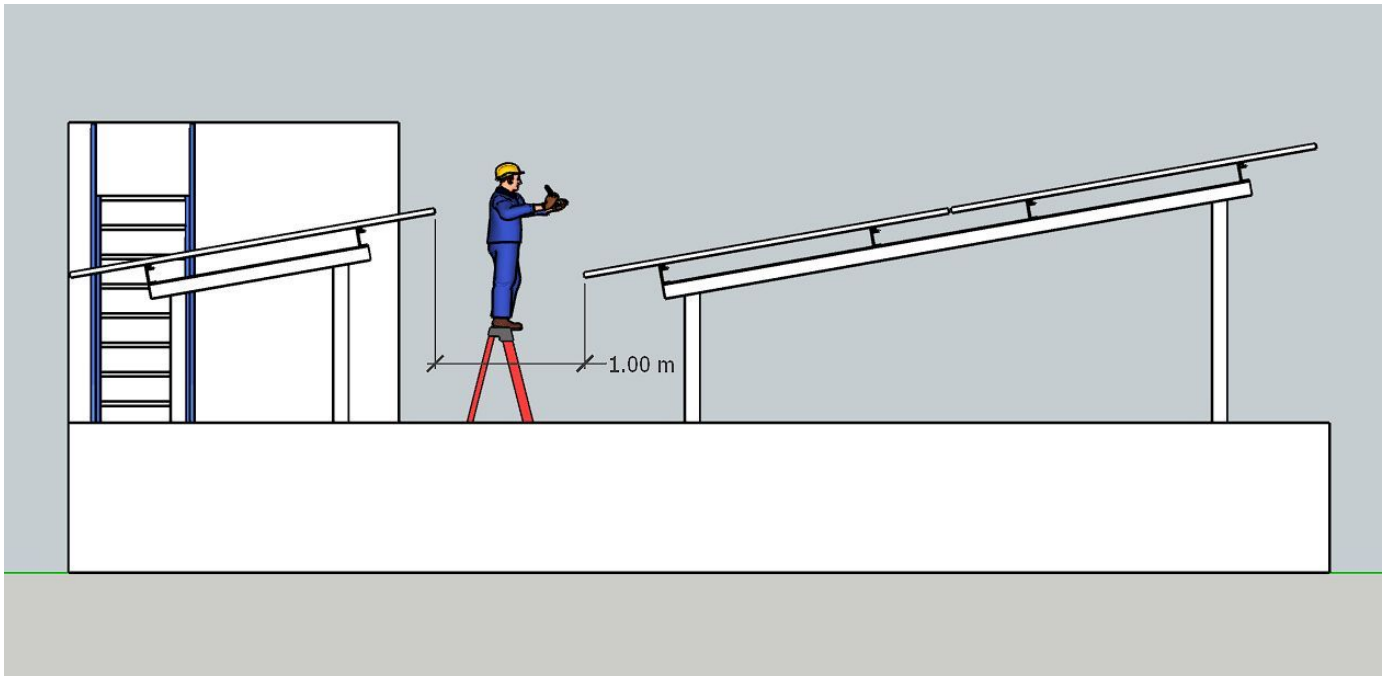

Structure Details

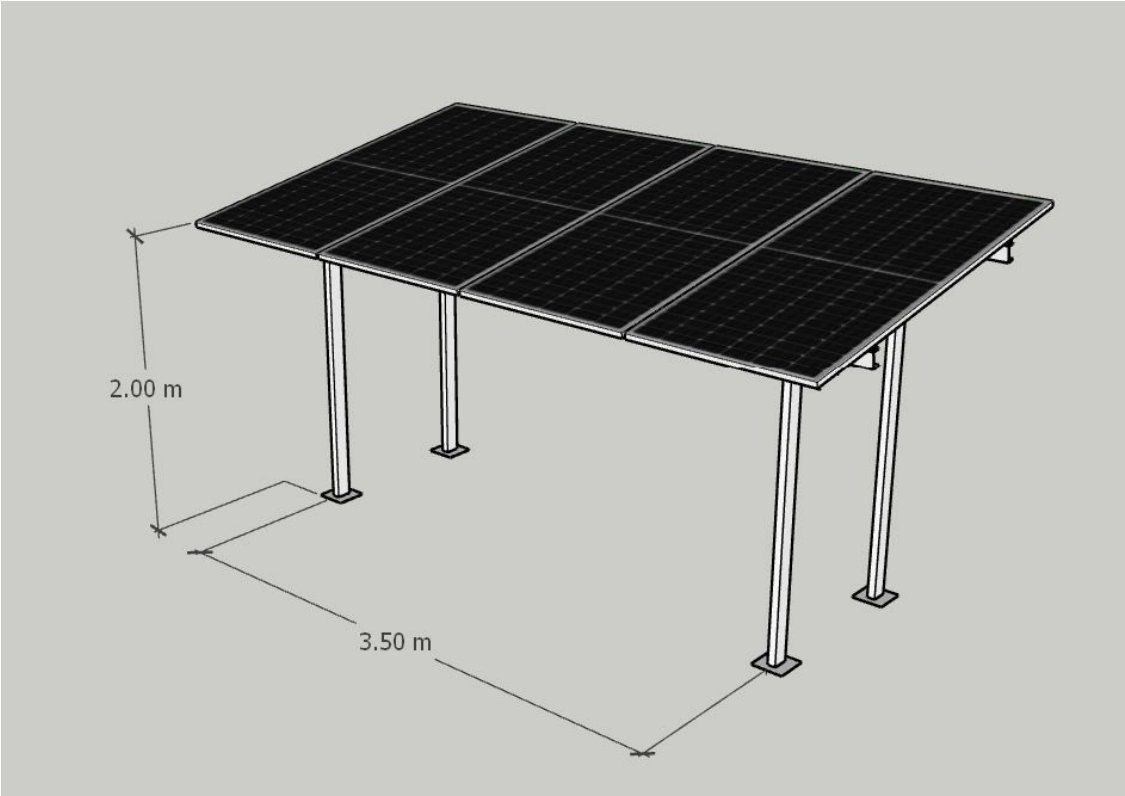


1P4 structure - 1No.

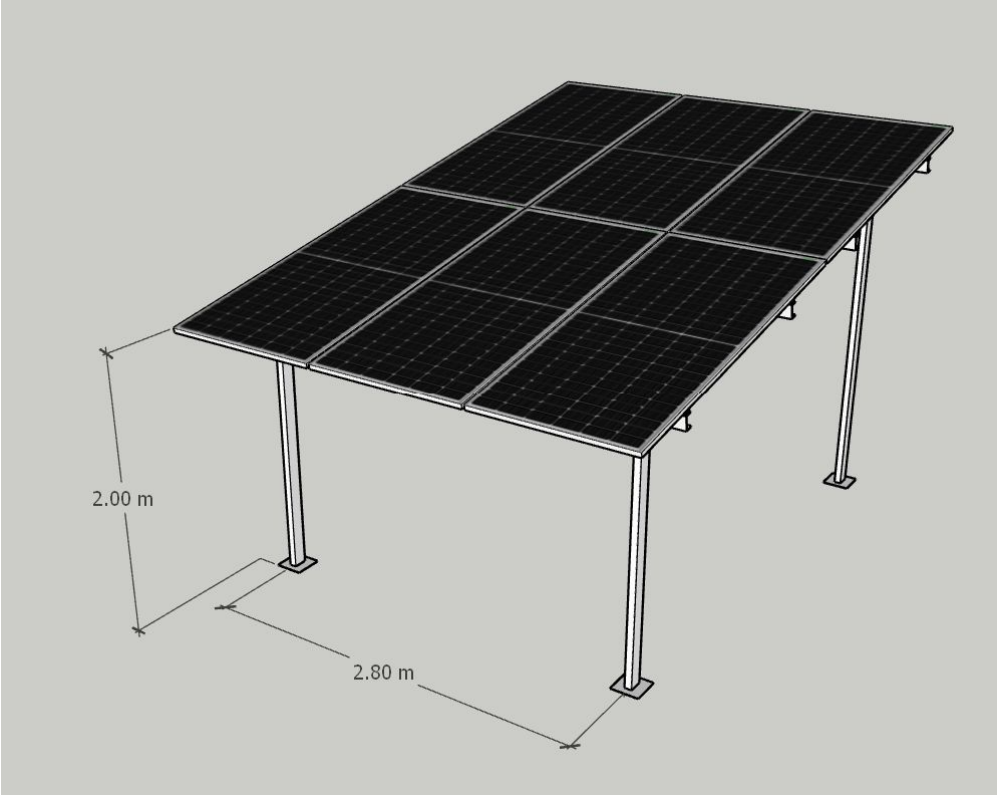


2P3 structure - 1No.

Building Exterior

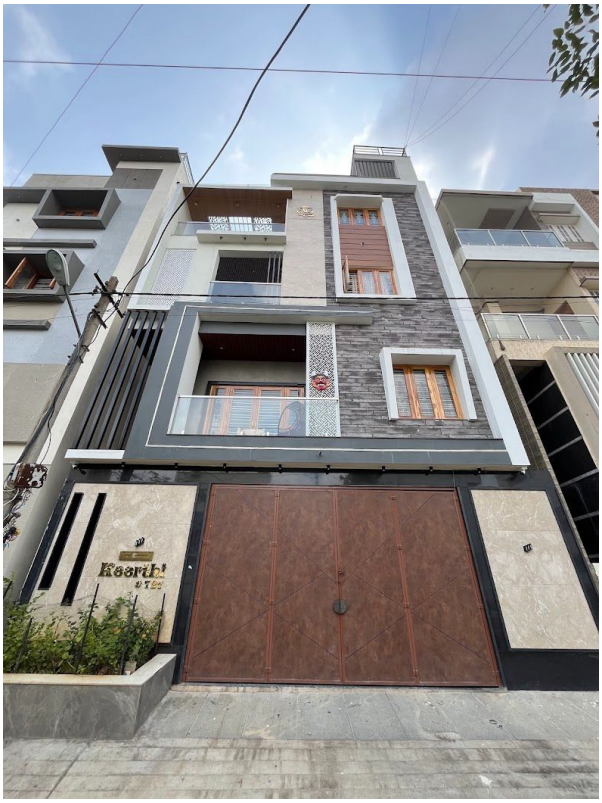


Material Delivery Route



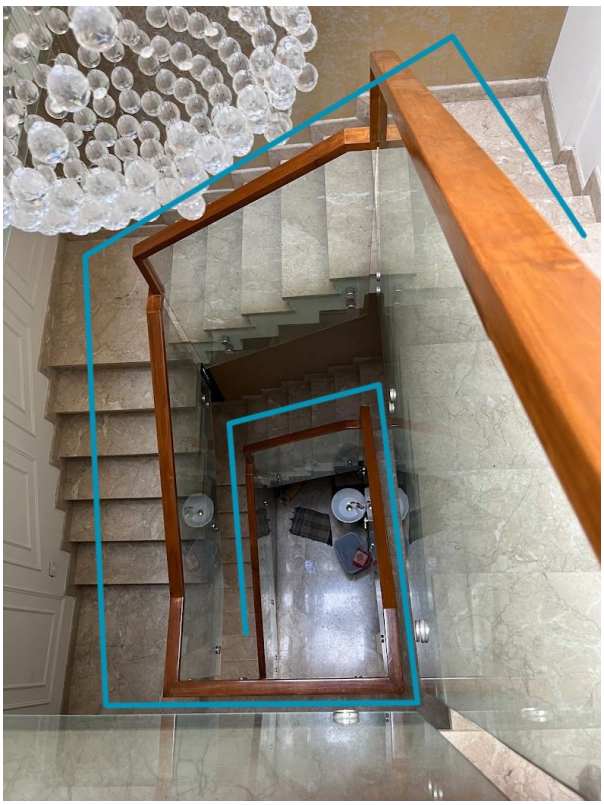

This route (using staircase) will be followed to carry all items.

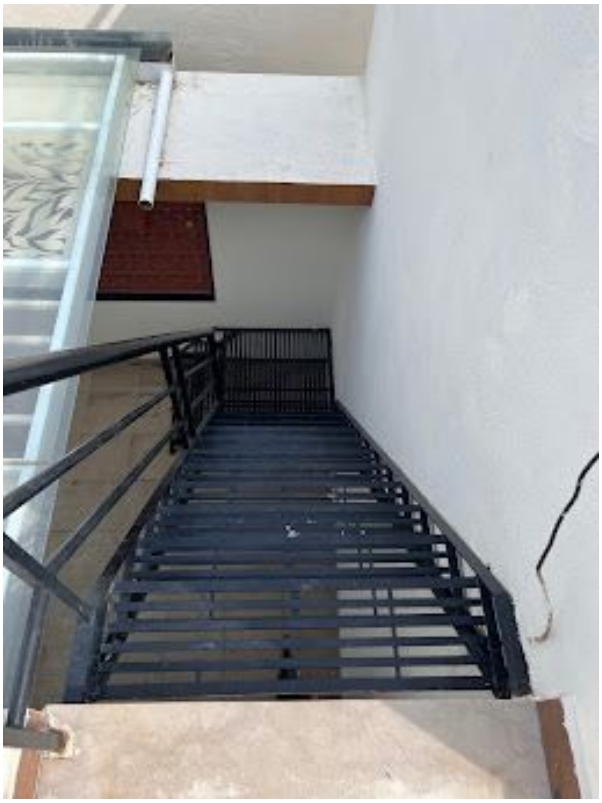

Staircase Details



Material Storage




Proposed PV Area




Cable Routing



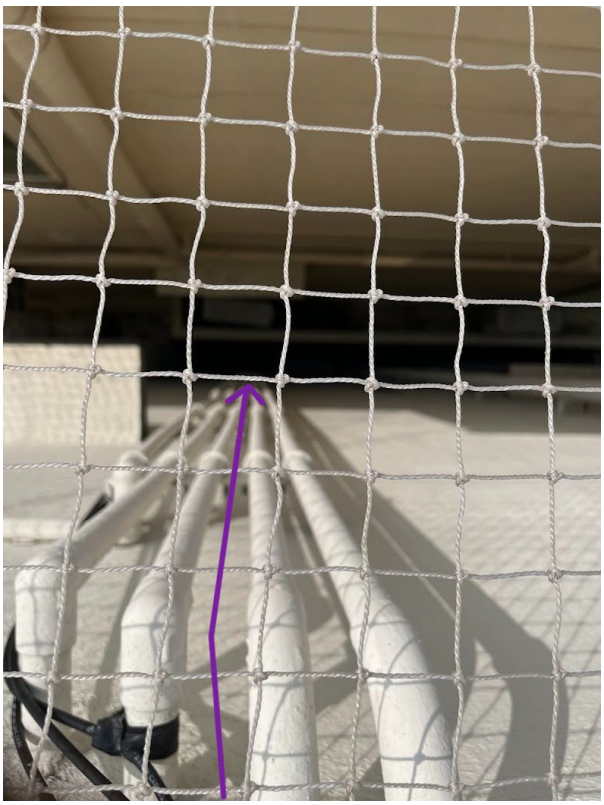




Conduit

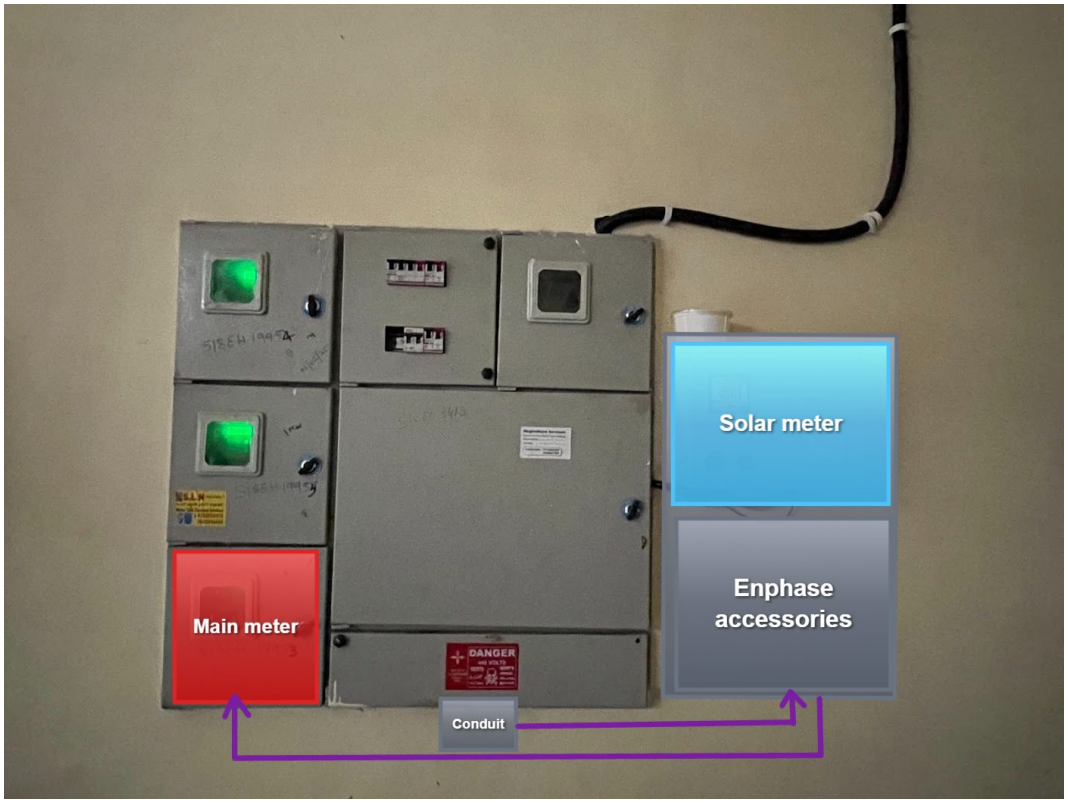
Solar meter
Enphase accessories
Main meter
DANGER
Conduit




Earthing Routing







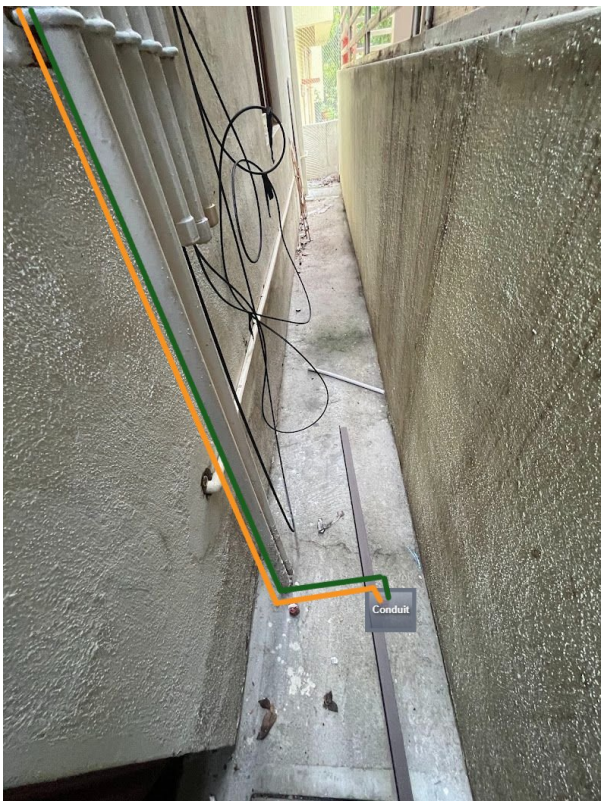

Earthing work has already completed, and the earthing cables have left in this area for connection.

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	Earthing work has already completed.

Customer Scope

#	Observation
1	Wi-Fi up to Inverter location.
2	The solar water heater must be relocated before the solar installation.
3	Provision shall be made to mount the Enphase accessories and solar meter box by relocating the existing motor starter to a different location.
4	6 sq.mm coper cables shall be provided for connecting to the existing earth pit.

THANK YOU

Dear Kiran Nag N J,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
