Technical Site Visit Report

Prepared for: John Kurian_Bhoopasandra_Sanjay Nagar_Non Subsidy_9.92kWp_String

PROJECT INFORMATION

Report Number	ESV-2026-0230
Project ID	CQEGL4LC
Project Name	John Kurian_Bhoopasandra_Sanjay Nagar_Non Subsidy_9.92kWp_String
Project Sector	Residential
Project Type	Without Subsidy
Sales Lead	Mahantayya
Site Address	No. 2, Dodda Krishnappa Layout Opp Sunrise English School Bhoopasandra, Sanjay Nagar Post Bangalore - 560094
GPS Coordinates	13.04433602273616, 77.57799915580453
Google Maps	https://www.google.com/maps?q=13.044336022736156,77.57799915580453
Visit Date	2026-10-13
Visited By	Charan P
Revision	Rev 0

CLIENT INFORMATION

Client Name	John Kurian
Contact	98807 09950

PROJECT DETAILS

Solar Rooftop System Type	On-Grid
System Capacity (kWp)	9.92
Sanction Load (kW)	10
Module Make & Capacity	Premier Bi-facial Non DCR and 620Wp
Module Length (mm)	2382

Module Width (mm)	1134
Number of Panels	16
Inverter Type	String
Inverter Brand	Deye 10 kW 3-Ph
Number of Inverters	1
Mounting Structure Type	Elevated

SITE INSPECTION CHECKLIST

General

#	Question	Answer	Notes
1	Can the delivery van/truck reach the material unloading point?	Yes	-
2	Are there any obstacles at the site that could hinder material lifting?	No	-
3	Where will the Inverter, DCDB, ACDB, Battery, etc. be located?	Near the main meter area.	-
4	Is a canopy required for protecting the Inverters/ACDB/DCDB?	details: Canopy is required for Inverter, ACDB and DCDB.	-
5	Did you discuss the location of the earth pits with the customer?	Yes, near the Main meter area.	-
6	Where is the Internet Router located?	On first floor	-
7	What's the Wi-Fi strength of the router near to the String inverter/Envoy?	3 bars	-
8	Did you pin the site location in your WhatsApp when you were at the site?	Yes	-

Roof Details

#	Question	Answer	Notes
1	What type of roof is present at the site?	RCC Flat Roof	-
2	Are there any obstructions on the roof that could affect the solar installation?	No	-
3	What is the angle of the panels? (in degrees)	10	-
4	In case of sloped roof, what is the slope angle of the roof? (in degrees)	N/A	-
5	On how many roofs at the site are we installing solar?	1	-
6	If it is a Tiled roof, what is underneath the tiles?	N/A	-
7	If it is a Tiled roof with MS or Wooden rafters, is it Single-tiled or Double-tiled?	N/A	-
8	What type of mounting structure is planned?	Elevated	*HDGI structure*
9	What is the orientation of the solar panels?	["South"]	-
10	How can the roof be accessed?	Staircase	-

#	Question	Answer	Notes
11	Is the building currently under construction?	No	-
12	In an under-construction building, are existing conduit pipes available for AC, DC cables, and earthing?	No	-
13	What is the height of the building and how many floors does it have?	10m with G+2 floor	-
14	Is the site photo matching with the building description?	Yes	-
15	Is there an overhead HT line passing within a 10-meter radius of the site?	No	-

Residential / Electrical

#	Question	Answer	Notes
1	What type of energy meter is currently installed?	Phase: Three Phase, Type: Digital	-
2	Is the Meter cubicle photo matching with the previous answer?	Yes	-
3	Has the termination point in the Main meter panel been identified?	Yes	-
4	Is the Termination Point easily visible or sealed?	Visible	-
5	Is a Lightning Arrestor (LA) already available at the site?	No	-
6	Is space available for CT within Energy meter panel?	N/A	-
7	In case of an Enphase system, is the distance between the farthest micro-inverter and IQ Gateway > 50m?	N/A	-
8	Provide details of the existing CT ratings (if applicable).	N/A	-
9	In Main meter panel, is empty space available for solar meter?	Yes	-
10	In Main meter panel, is empty space available to house the Enphase accessories or ACDB components?	N/A	-
11	Is there space available to dig DC, AC and LA earth pits?	Yes	-
12	What type of Earthing chamber needs to be installed at site? Is it Cement chamber or PVC chamber?	Cement chamber	-
12 a	What's the depth of the concrete?	-	-
13	In case of elevated structures, is an LA extension provided at the far end?	No	-
14	In case of elevated structures, is it with or without grouting?	With Grouting	-
15	Are there any challenges with respect to Installation and Maintenance activities?	No	-
16	Are there any safety risks associated with accessing the roof for installation?	No	-
17	Is space present in rooftop to store the panels?	Horizontally sleeping	-
18	In case of sloped roof MS structure, provide the dimension of rafter to rafter, purlin to purlin.	N/A	-
19	Is ventilation available in the battery location?	N/A	-
20	Is Battery wall mounted or stand mounted?	N/A	-
21	Should the Inverters/ACDB/DCDB be installed on a metal grill or wall mount?	Wall mount	-
22	Provide the dimensions for solar meter cubicle placement (L x W of wall).	length: 650,	-

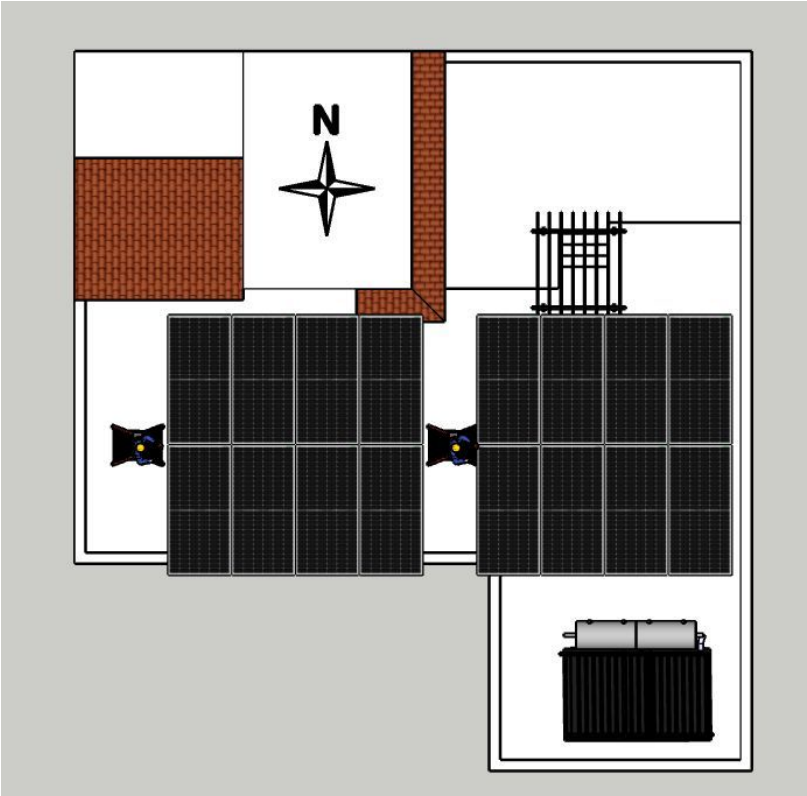
#	Question	Answer	Notes
		width: 650	
23	Provide the dimension for earth pits location (L x W of available space).	length: 3000, width: 1000	-
24	Is LAN cable under customer scope?	No	-
25	Is there any shadow that affects the solar installation?	No	-
26	Is there any trench work to be done to carry the AC cable to the meter location?	No	-


PHOTO DOCUMENTATION


Cable Routing Legend


Legend	Description
	Proposed PV Module Array
	Main Meter Location
	Solar Meter
	Battery
	Inverter
	Other Equipment
	DC Cable
	AC Cable
	Material Shifting
	DC Earthing Cable
	AC Earthing Cable
	LA Cable
	DC Earth Pit
	AC Earth Pit
	LA Pit
	LA

Site Layout


N

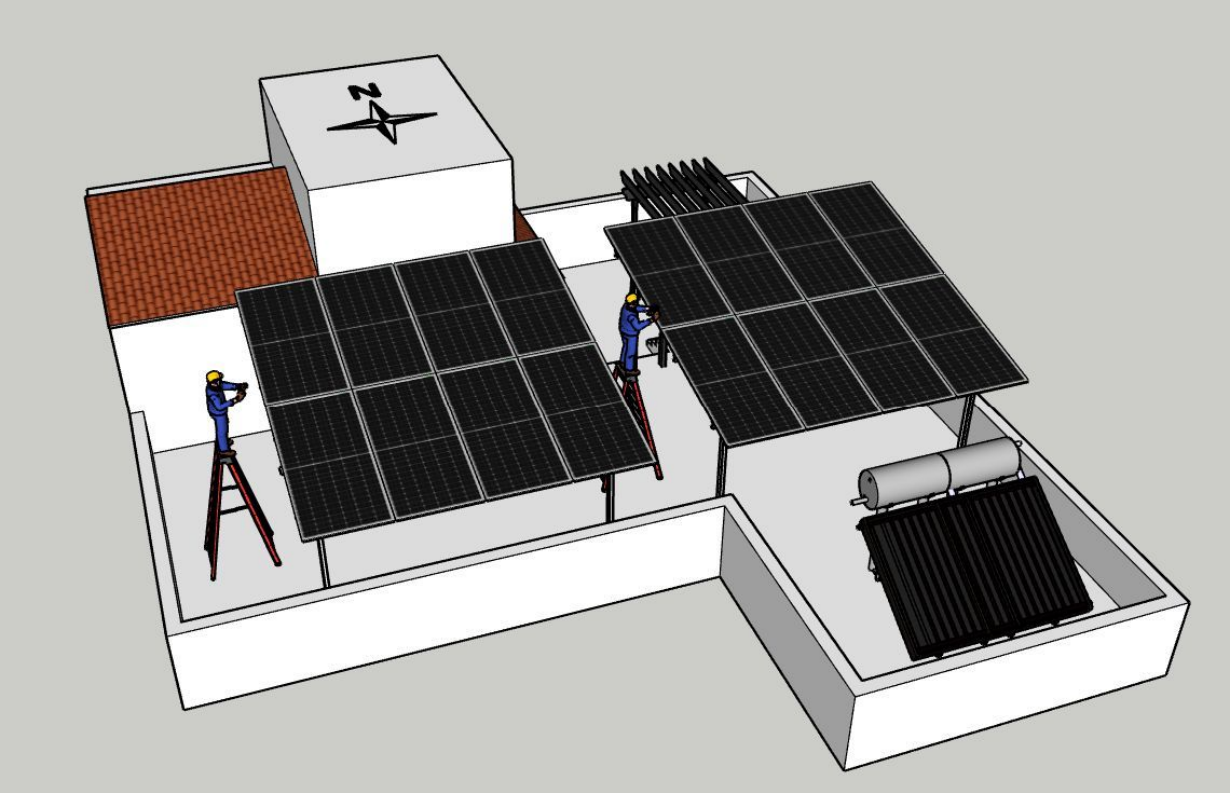
N

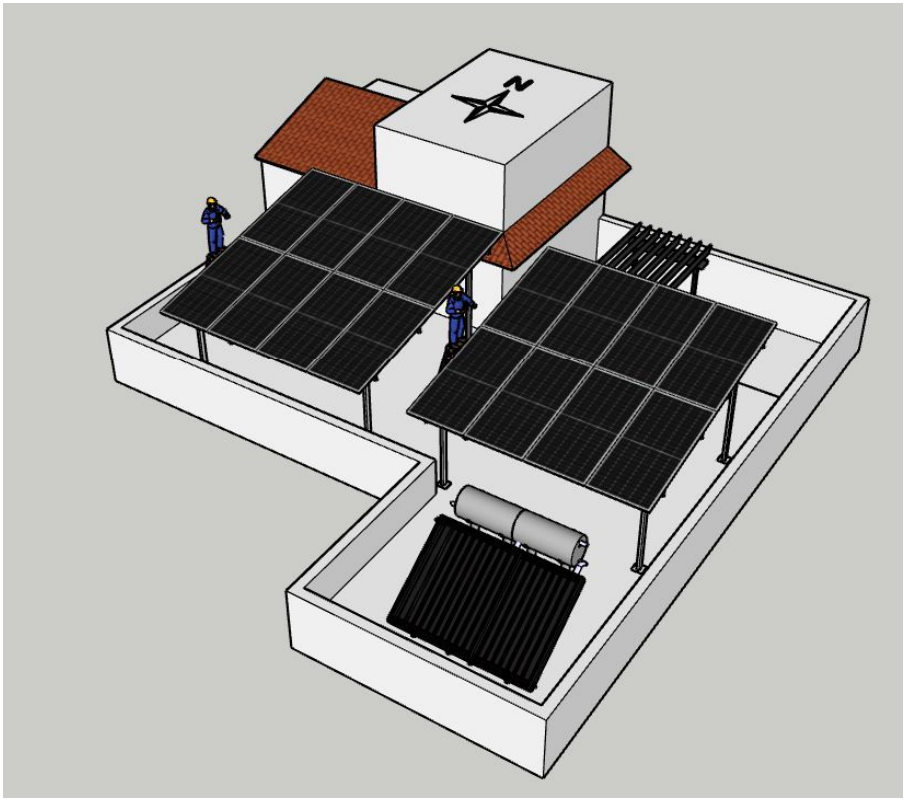

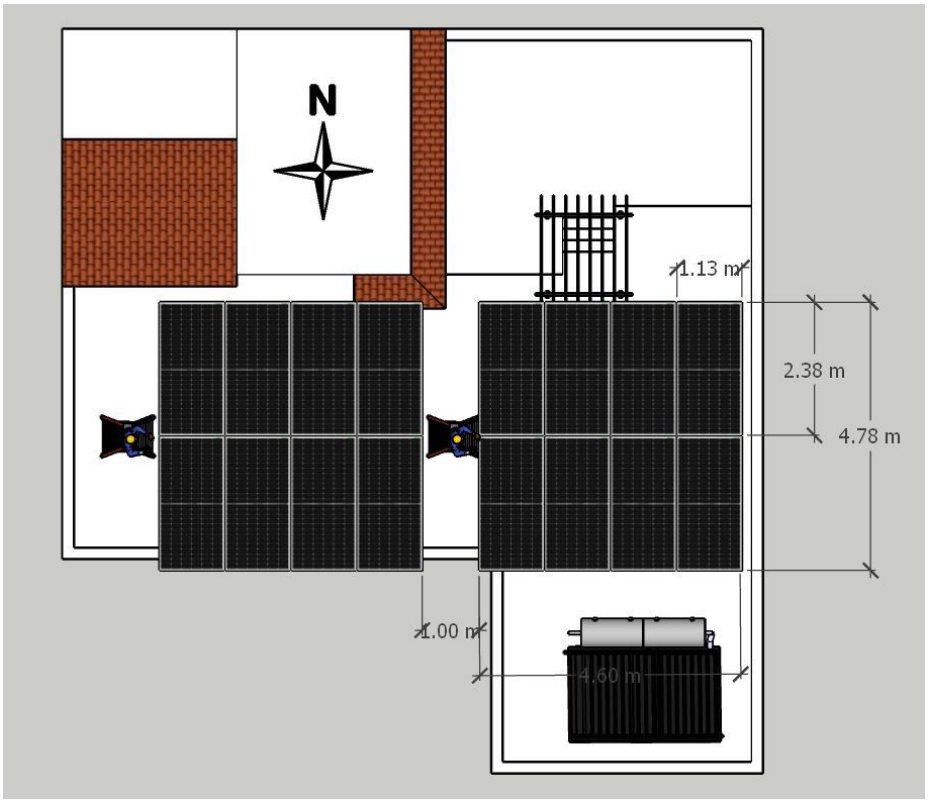

Building Exterior




Material Delivery Route








This route (using staircase) will be followed to carry all items.

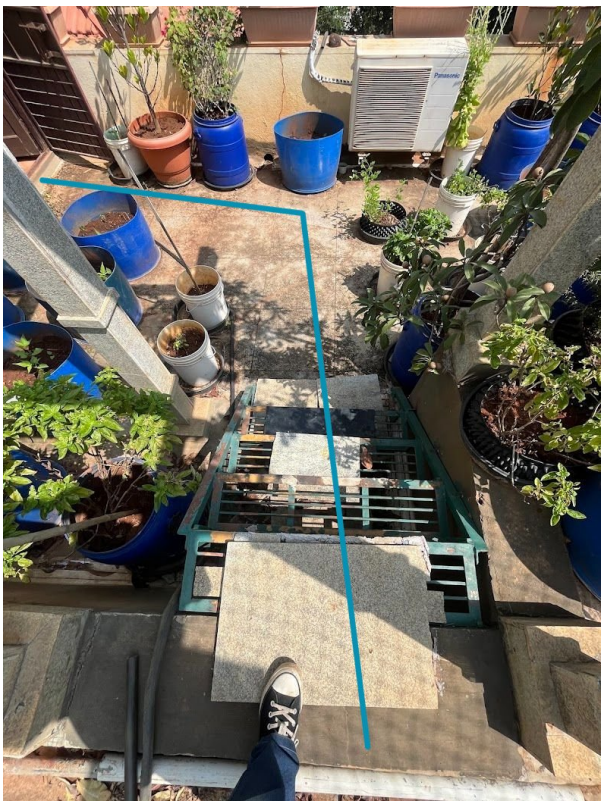



Staircase Details

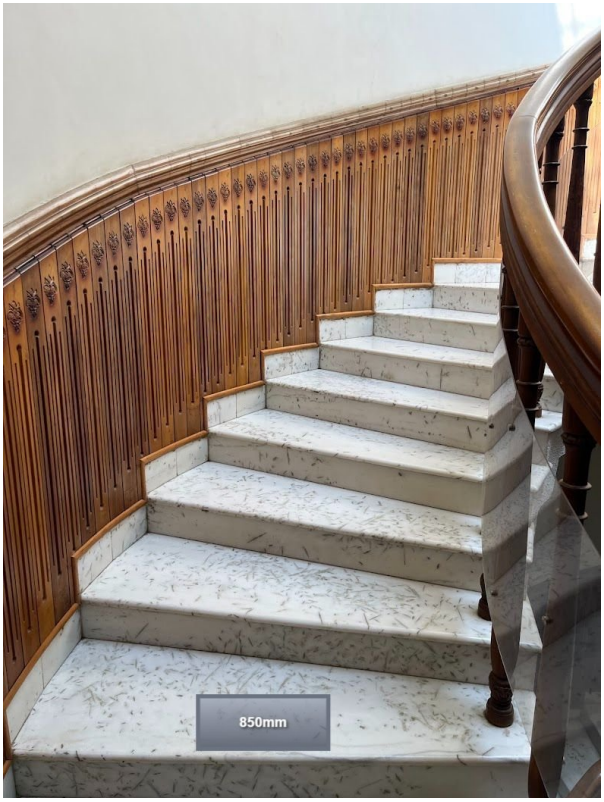

Material Storage




Proposed PV Area





Cable Routing




PV modules

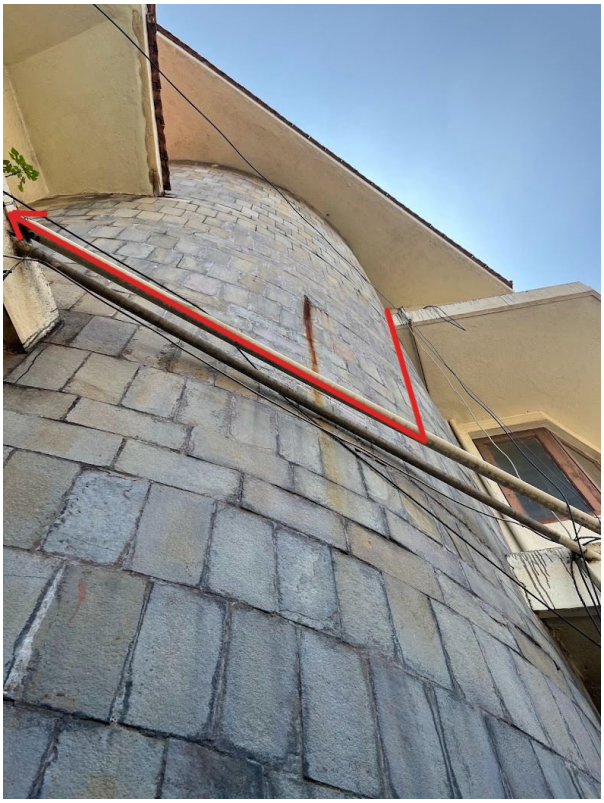

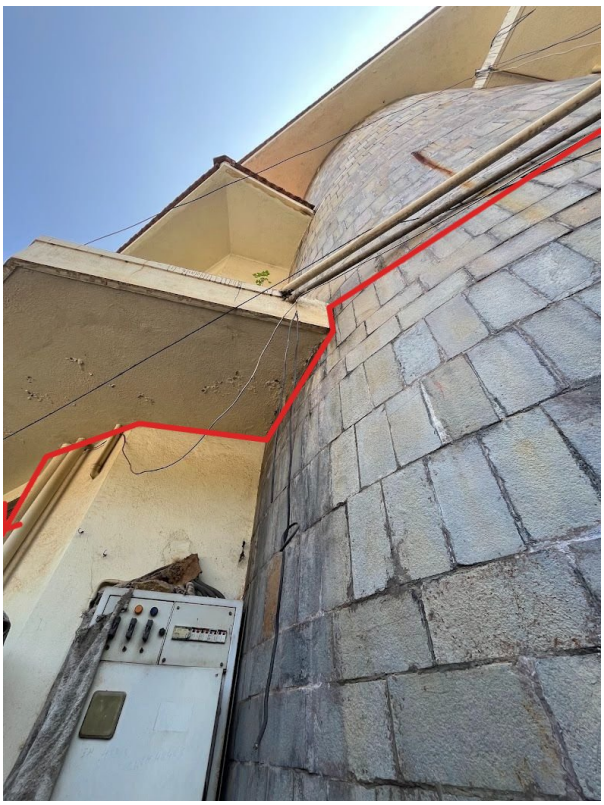

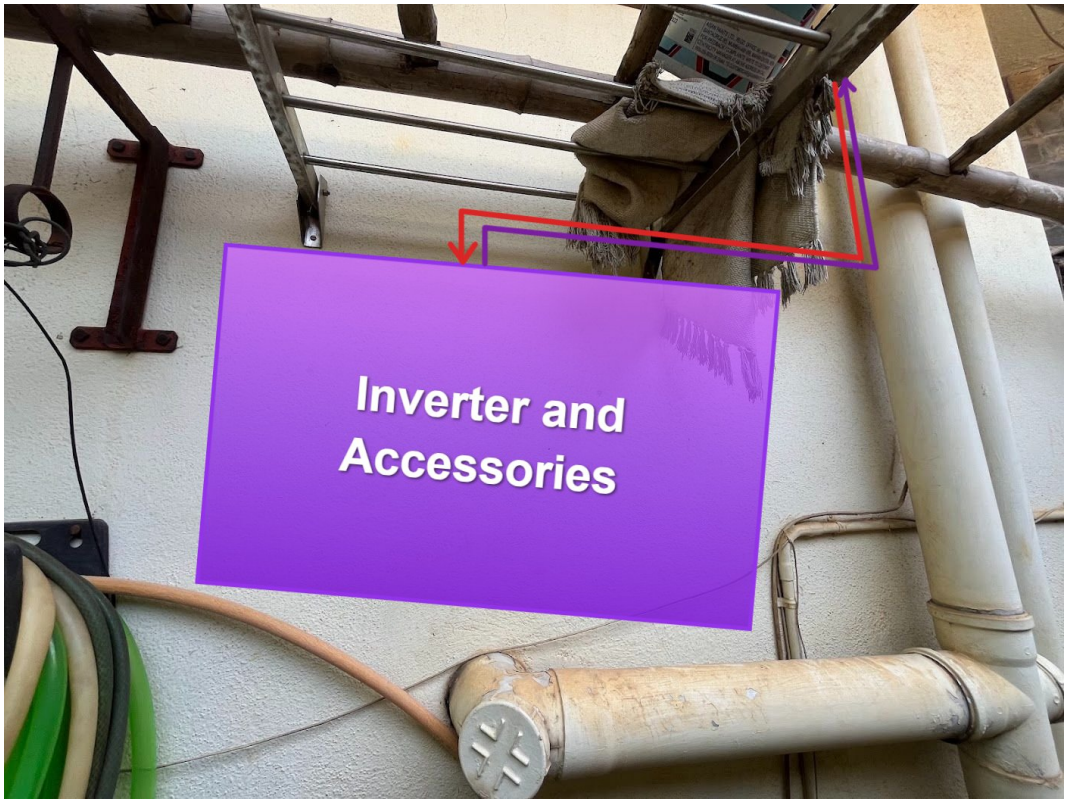
Inverter and
Accessories







Earthing Routing


PV modules



LA
PV modules

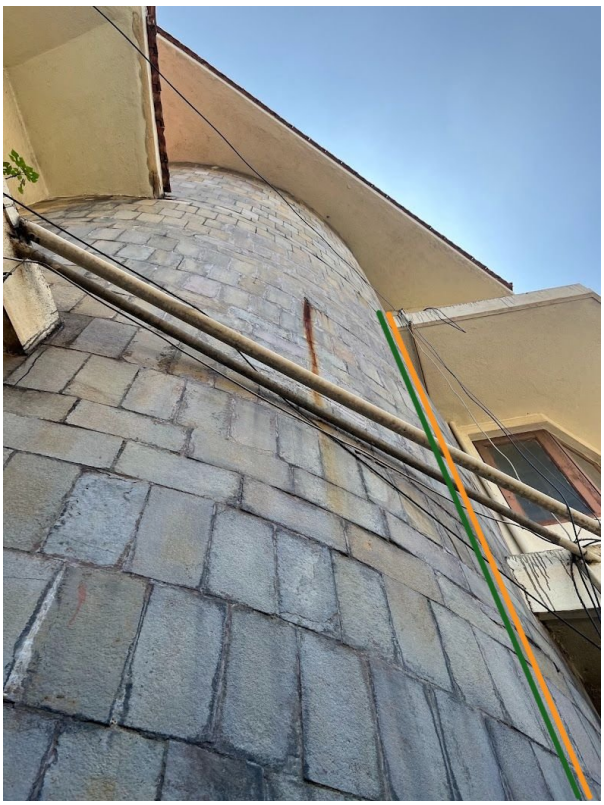

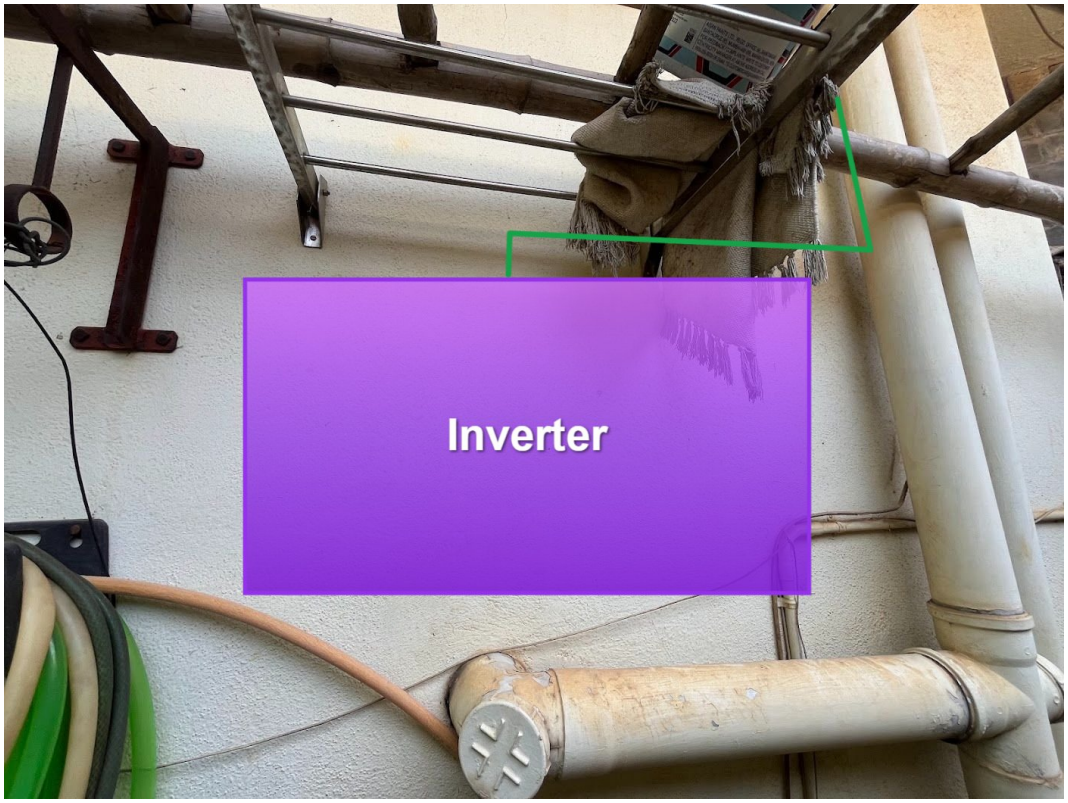
Inverter




AC Earth Pit

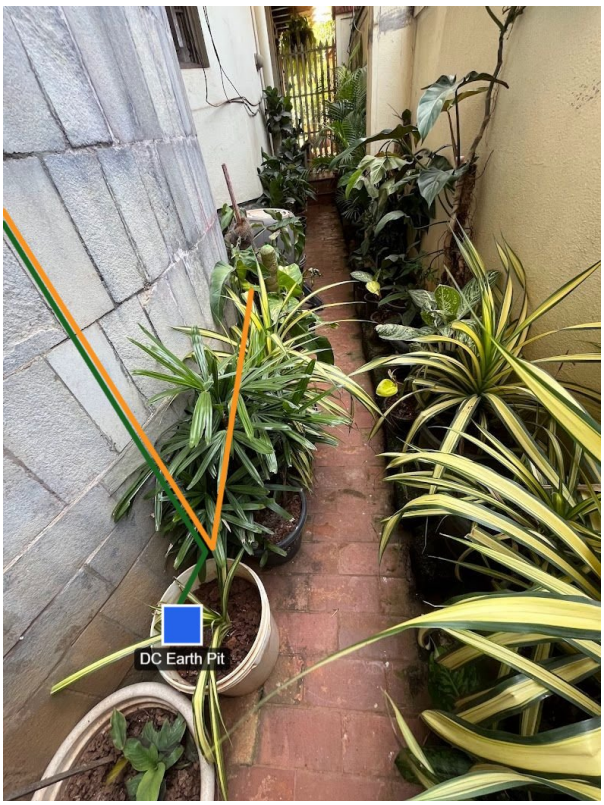
DC Earth Pit


LA Pit

OBSERVATIONS & RECOMMENDATIONS

EcoSoch Scope

#	Observation
1	The existing main meter box can be used to install the solar meter, as it has sufficient space to accommodate both meters.

Customer Scope

#	Observation
1	Wi-Fi up to Inverter location.
2	The solar water heater must be relocated before the solar panel installation.
3	The pergola must be removed before installing the solar panel structure.

THANK YOU

Dear John Kurian,

Thank you for choosing EcoSoch Solar for your solar installation. We appreciate your trust in us and your commitment to sustainable energy. Our team is dedicated to ensuring a seamless installation experience and long-term performance of your solar system.

Should you have any questions or require further assistance, please do not hesitate to reach out to us.

Warm Regards,
Team EcoSoch

& Did You Know?

The Sun burns 600 million tonnes of hydrogen per second — and your panels get a share.

EcoSoch Solar Pvt. Ltd.
#940, Sha Arcade, 2nd Phase, NTI Layout, Kodigehalli, Bengaluru 560097
www.ecosoch.com | info@ecosoch.com
